

SUBJECT: ACCEPTANCE OF PROJECT – MICRO-SURFACING PROJECT (DATE AVENUE, HENDERSON AVENUE, INDIANA STREET, JAYE STREET AND MAIN STREET)

SOURCE: Public Works Department - Engineering Division

COMMENT: VSS International, Inc. has completed the 2014 Micro-Surfacing Project per plans and specifications. The project consisted of the removal and replacement of distressed asphalt concrete (Date Avenue), installation of a thin asphalt overlay and new pavement markings. The project consisted of micro-surfacing Date Avenue from Main Street to Orange Avenue, Henderson Avenue from Jaye Street to Main Street, Jaye Street from SR 190 to Springville Avenue, and Main Street from Yates Avenue to SR 190.

Staff carefully tracks construction costs of all Capital Improvements Projects and reports project construction expenditures when the project is accepted by the City Council. On June 17, 2014, City Council authorized expenditure of \$375,284.33 for construction, construction management and quality control services for the Micro-Surfacing Project. The following itemizes the construction-related costs in two categories: 1) the construction contract, and 2) a combination of construction management and quality control.

- 1) Final construction cost is \$342,577.00.
- 2) Construction management and quality control costs are \$10,384.76.

Total project construction costs equate to \$352,961.76, which is less than the \$375,284.33 overall budget approved by Council at the time of award.

Measure "R" is the funding source for the Micro-Surfacing Project and was approved in the 2013/2014 Annual Budget and re-appropriated in the 2014/2015 Annual Budget.

VSS International Inc. requests that the City accept the project as complete. Staff reviewed the work and found it acceptable.

RECOMMENDATION: That City Council:

1. Accept the project as complete;
2. Authorize the filing of the Notice of Completion; and
3. Authorize the release of the 5% retention thirty-five (35) days after recordation, provided no stop notices have been filed.

ATTACHMENT: Locator Map

P:\pubworks\General\Council\Acceptance of Project - Micro-Surfacing Project 2014 - 2014-11-04.doc

Dir By Appropriated/Funded MP CM J


Item No. 6

2013-2014 MICRO-SURFACING PROJECT


CITY PROJECT NO. 89-9167




SCALE: N.T.S

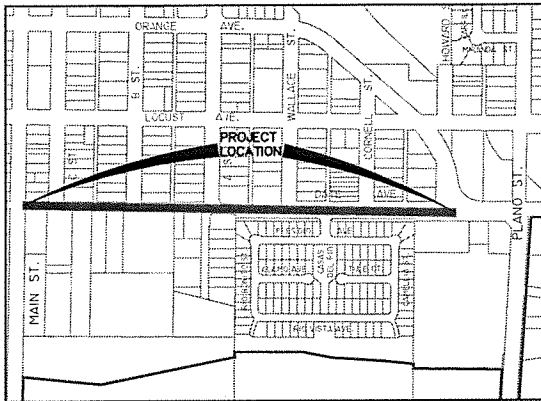


DATE AVENUE

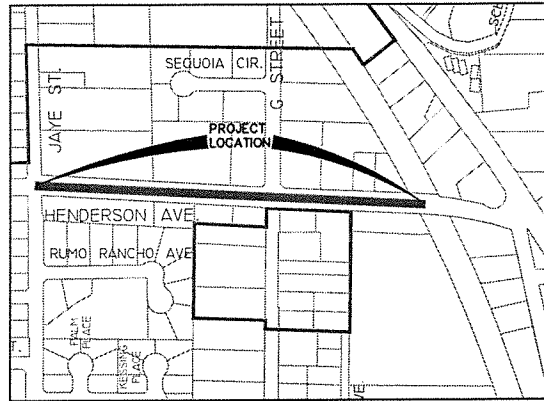


HENDERSON AVENUE

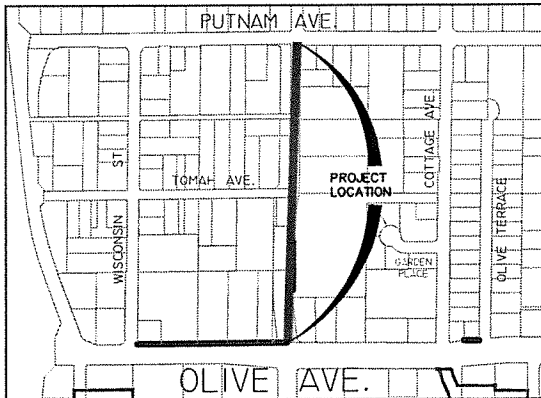

INDIANA STREET

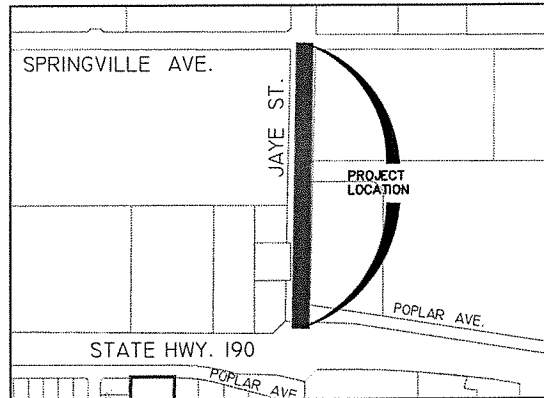

JAYE STREET

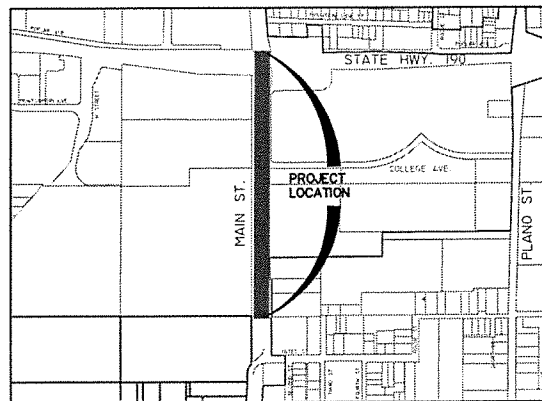

MAIN STREET

CITY OF PORTERVILLE
 ENGINEERING DIVISION
 291 NORTH MAIN STREET
 PORTERVILLE, CA. 93257
 (559) 782-7482

2013 -2014 MICRO
 SURFACING PROJECT
 LOCATOR MAP

DRAWN BY	VS
CHECKED BY	MKR
SCALE	N.T.S.
DATE	5/06/2014

SHEET
 1
 OF
 1
